



Commonwealth of Massachusetts

Title 5 Official Inspection Form

Subsurface Sewage Disposal System Form - Not for Voluntary Assessments

950 Falmouth Road units 1-5

Property Address

South Cape Resort - Latour Group

Owner's Name

Mashpee

Ma

02649

9/24/2024

City/Town

State


Zip Code

Date of Inspection

Owner information is required for every page.

Inspection results must be submitted on this form. Inspection forms may not be altered in any way. Please see completeness checklist at the end of the form.

Important: When filling out forms on the computer, use only the tab key to move your cursor - do not use the return key.



A. Inspector Information

Chad Hathaway

Name of Inspector

Hathaway Septic Service LLC

Company Name

P.O.Box 151

Company Address

Forestdale

City/Town

Ma

02644

State

Zip Code

774 274 2581

12866

Telephone Number

License Number

B. Certification

I certify that: I am a DEP approved system inspector in full compliance with Section 15.340 of Title 5 (310 CMR 15.000); I have personally inspected the sewage disposal system at the property address listed above; the information reported below is true, accurate and complete as of the time of my inspection; and the inspection was performed based on my training and experience in the proper function and maintenance of on-site sewage disposal systems. After conducting this inspection I have determined that the system:

1. Passes
2. Conditionally Passes
3. Needs Further Evaluation by the Local Approving Authority
4. Fails


Inspector's Signature

9/24/2024

Date

The system inspector shall submit a copy of this inspection report to the Approving Authority (Board of Health or DEP) within 30 days of completing this inspection. If the system has a design flow of 10,000 gpd or greater, the inspector and the system owner shall submit the report to the appropriate regional office of the DEP. The original form should be sent to the system owner and copies sent to the buyer, if applicable, and the approving authority.

Please note: This report only describes conditions at the time of inspection and under the conditions of use at that time. This inspection does not address how the system will perform in the future under the same or different conditions of use.



Title 5 Official Inspection Form

Subsurface Sewage Disposal System Form - Not for Voluntary Assessments

950 Falmouth Road units 1-5

Property Address

South Cape Resort - Latour Group

Owner's Name

Mashpee

Ma

02649

9/24/2024

City/Town

State

Zip Code

Date of Inspection

Owner information is required for every page.

C. Inspection Summary

Inspection Summary: Complete 1, 2, 3, or 5 and all of 4 and 6.

1) System Passes:

I have not found any information which indicates that any of the failure criteria described in 310 CMR 15.303 or in 310 CMR 15.304 exist. Any failure criteria not evaluated are indicated below.

Comments:

No failure criteria encountered during inspection. All covers at grade or within 6" of grade or within 6" of final grade

2) System Conditionally Passes:

One or more system components as described in the "Conditional Pass" section need to be replaced or repaired. The system, upon completion of the replacement or repair, as approved by the Board of Health, will pass.

Check the box for "yes", "no" or "not determined" (Y, N, ND) for the following statements. If "not determined," please explain.

The septic tank is metal and over 20 years old* or the septic tank (whether metal or not) is structurally unsound, exhibits substantial infiltration or exfiltration or tank failure is imminent. System will pass inspection if the existing tank is replaced with a complying septic tank as approved by the Board of Health.

* A metal septic tank will pass inspection if it is structurally sound, not leaking and if a Certificate of Compliance indicating that the tank is less than 20 years old is available.

Y N ND (Explain below):



Title 5 Official Inspection Form

Subsurface Sewage Disposal System Form - Not for Voluntary Assessments

950 Falmouth Road units 1-5

Property Address

South Cape Resort - Latour Group

Owner's Name

Mashpee

Ma

02649

9/24/2024

City/Town

State

Zip Code

Date of Inspection

Owner information is required for every page.

C. Inspection Summary (cont.)

2) System Conditionally Passes (cont.):

Pump Chamber pumps/alarms not operational. System will pass with Board of Health approval if pumps/alarms are repaired.

Observation of sewage backup or break out or high static water level in the distribution box due to broken or obstructed pipe(s) or due to a broken, settled or uneven distribution box. System will pass inspection if (with approval of Board of Health):

broken pipe(s) are replaced Y N ND (Explain below):

obstruction is removed Y N ND (Explain below):

distribution box is leveled or replaced Y N ND (Explain below):

The system required pumping more than 4 times a year due to broken or obstructed pipe(s). The system will pass inspection if (with approval of the Board of Health):

broken pipe(s) are replaced Y N ND (Explain below):

obstruction is removed Y N ND (Explain below):

3) Further Evaluation is Required by the Board of Health:

Conditions exist which require further evaluation by the Board of Health in order to determine if the system is failing to protect public health, safety or the environment.

a. System will pass unless Board of Health determines in accordance with 310 CMR 15.303(1)(b) that the system is not functioning in a manner which will protect public health, safety and the environment:



Title 5 Official Inspection Form

Subsurface Sewage Disposal System Form - Not for Voluntary Assessments

950 Falmouth Road units 1-5

Property Address

South Cape Resort - Latour Group

Owner's Name

Mashpee

Ma

02649

9/24/2024

City/Town

State

Zip Code

Date of Inspection

Owner information is required for every page.

C. Inspection Summary (cont.)

- Cesspool or privy is within 50 feet of a surface water
- Cesspool or privy is within 50 feet of a bordering vegetated wetland or a salt marsh

b. System will fail unless the Board of Health (and Public Water Supplier, if any) determines that the system is functioning in a manner that protects the public health, safety and environment:

- The system has a septic tank and soil absorption system (SAS) and the SAS is within 100 feet of a surface water supply or tributary to a surface water supply.
- The system has a septic tank and SAS and the SAS is within a Zone 1 of a public water supply.
- The system has a septic tank and SAS and the SAS is within 50 feet of a private water supply well.
- The system has a septic tank and SAS and the SAS is less than 100 feet but 50 feet or more from a private water supply well**.

Method used to determine distance: _____

** This system passes if the well water analysis, performed at a DEP certified laboratory, for fecal coliform bacteria indicates absent and the presence of ammonia nitrogen and nitrate nitrogen is equal to or less than 5 ppm, provided that no other failure criteria are triggered. A copy of the analysis must be attached to this form.

c. Other:

4) System Failure Criteria Applicable to All Systems:

You must indicate "Yes" or "No" to each of the following for all inspections:

Yes No

Backup of sewage into facility or system component due to overloaded or clogged SAS or cesspool

Discharge or ponding of effluent to the surface of the ground or surface waters due to an overloaded or clogged SAS or cesspool



Title 5 Official Inspection Form

Subsurface Sewage Disposal System Form - Not for Voluntary Assessments

950 Falmouth Road units 1-5

Property Address

South Cape Resort - Latour Group

Owner's Name

Mashpee

Ma

02649

9/24/2024

City/Town

State

Zip Code

Date of Inspection

Owner information is required for every page.

C. Inspection Summary (cont.)

4) System Failure Criteria Applicable to All Systems: (cont.)

- | Yes | No | |
|--------------------------|-------------------------------------|---|
| <input type="checkbox"/> | <input checked="" type="checkbox"/> | Static liquid level in the distribution box above outlet invert due to an overloaded or clogged SAS or cesspool |
| <input type="checkbox"/> | <input checked="" type="checkbox"/> | Liquid depth in cesspool is less than 6" below invert or available volume is less than 1/2 day flow |
| <input type="checkbox"/> | <input checked="" type="checkbox"/> | Required pumping more than 4 times in the last year NOT due to clogged or obstructed pipe(s). Number of times pumped: _____. |
| <input type="checkbox"/> | <input checked="" type="checkbox"/> | Any portion of the SAS, cesspool or privy is below high ground water elevation. |
| <input type="checkbox"/> | <input checked="" type="checkbox"/> | Any portion of cesspool or privy is within 100 feet of a surface water supply or tributary to a surface water supply. |
| <input type="checkbox"/> | <input checked="" type="checkbox"/> | Any portion of a cesspool or privy is within a Zone 1 of a public water supply well. |
| <input type="checkbox"/> | <input checked="" type="checkbox"/> | Any portion of a cesspool or privy is within 50 feet of a private water supply well. |
| <input type="checkbox"/> | <input checked="" type="checkbox"/> | Any portion of a cesspool or privy is less than 100 feet but greater than 50 feet from a private water supply well with no acceptable water quality analysis. [This system passes if the well water analysis, performed at a DEP certified laboratory, for fecal coliform bacteria indicates absent and the presence of ammonia nitrogen and nitrate nitrogen is equal to or less than 5 ppm, provided that no other failure criteria are triggered. A copy of the analysis and chain of custody must be attached to this form.] |
| <input type="checkbox"/> | <input checked="" type="checkbox"/> | The system is a cesspool serving a facility with a design flow of 2000 gpd-10,000 gpd. |
| <input type="checkbox"/> | <input checked="" type="checkbox"/> | The system fails. I have determined that one or more of the above failure criteria exist as described in 310 CMR 15.303, therefore the system fails. The system owner should contact the Board of Health to determine what will be necessary to correct the failure. |

5) Large Systems: To be considered a large system the system must serve a facility with a design flow of 10,000 gpd to 15,000 gpd.

For large systems, you must indicate either "yes" or "no" to each of the following, in addition to the questions in Section C.4.

- | Yes | No | |
|--------------------------|--------------------------|--|
| <input type="checkbox"/> | <input type="checkbox"/> | the system is within 400 feet of a surface drinking water supply |
| <input type="checkbox"/> | <input type="checkbox"/> | the system is within 200 feet of a tributary to a surface drinking water supply |
| <input type="checkbox"/> | <input type="checkbox"/> | the system is located in a nitrogen sensitive area (Interim Wellhead Protection Area – IWPA) or a mapped Zone II of a public water supply well |



Title 5 Official Inspection Form

Subsurface Sewage Disposal System Form - Not for Voluntary Assessments

950 Falmouth Road units 1-5

Property Address

South Cape Resort - Latour Group

Owner's Name

Mashpee

Ma

02649

9/24/2024

City/Town

State

Zip Code

Date of Inspection

Owner information is required for every page.

C. Inspection Summary (cont.)

If you have answered "yes" to any question in Section C.5 the system is considered a significant threat, or answered "yes" to any question in Section C.4 above the large system has failed. The owner or operator of any large system considered a significant threat under Section C.5 or failed under Section C.4 shall upgrade the system in accordance with 310 CMR 15.304. The system owner should contact the appropriate regional office of the Department.

6. You must indicate "yes" or "no" for each of the following for *all* inspections:

- | Yes | No | |
|-------------------------------------|-------------------------------------|---|
| <input checked="" type="checkbox"/> | <input type="checkbox"/> | Pumping information was provided by the owner, occupant, or Board of Health |
| <input type="checkbox"/> | <input checked="" type="checkbox"/> | Were any of the system components pumped out in the previous two weeks? |
| <input checked="" type="checkbox"/> | <input type="checkbox"/> | Has the system received normal flows in the previous two week period? |
| <input type="checkbox"/> | <input checked="" type="checkbox"/> | Have large volumes of water been introduced to the system recently or as part of this inspection? |
| <input checked="" type="checkbox"/> | <input type="checkbox"/> | Were as built plans of the system obtained and examined? (If they were not available note as N/A) |
| <input checked="" type="checkbox"/> | <input type="checkbox"/> | Was the facility or dwelling inspected for signs of sewage back up? |
| <input checked="" type="checkbox"/> | <input type="checkbox"/> | Was the site inspected for signs of break out? |
| <input checked="" type="checkbox"/> | <input type="checkbox"/> | Were all system components, excluding the SAS, located on site? |
| <input checked="" type="checkbox"/> | <input type="checkbox"/> | Were the septic tank manholes uncovered, opened, and the interior of the tank inspected for the condition of the baffles or tees, material of construction, dimensions, depth of liquid, depth of sludge and depth of scum? |
| <input checked="" type="checkbox"/> | <input type="checkbox"/> | Was the facility owner (and occupants if different from owner) provided with information on the proper maintenance of subsurface sewage disposal systems? The size and location of the Soil Absorption System (SAS) on the site has been determined based on: |
| <input checked="" type="checkbox"/> | <input type="checkbox"/> | Existing information. For example, a plan at the Board of Health. |
| <input type="checkbox"/> | <input checked="" type="checkbox"/> | Determined in the field (if any of the failure criteria related to Part C is at issue approximation of distance is unacceptable) [310 CMR 15.302(5)] |



Title 5 Official Inspection Form

Subsurface Sewage Disposal System Form - Not for Voluntary Assessments

950 Falmouth Road units 1-5

Property Address

South Cape Resort - Latour Group

Owner's Name

Mashpee

Ma

02649

9/24/2024

City/Town

State

Zip Code

Date of Inspection

Owner information is required for every page.

D. System Information

1. Residential Flow Conditions:

Number of bedrooms (design): 11 Number of bedrooms (actual): 10

DESIGN flow based on 310 CMR 15.203 (for example: 110 gpd x # of bedrooms): 1100

Description:
per plans and files

Number of current residents: varies

Does residence have a garbage grinder? Yes No

Does residence have a water treatment unit? Yes No

If yes, discharges to: _____

Is laundry on a separate sewage system? (Include laundry system inspection information in this report.) Yes No

Laundry system inspected? Yes No

Seasonal use? Yes No

Water meter readings, if available (last 2 years usage (gpd)): _____

Detail:

Sump pump? Yes No

Last date of occupancy: unknown
Date



Commonwealth of Massachusetts
Title 5 Official Inspection Form
 Subsurface Sewage Disposal System Form - Not for Voluntary Assessments

Owner information is required for every page.

950 Falmouth Road units 1-5
 Property Address
 South Cape Resort - Latour Group
 Owner's Name
 Mashpee Ma 02649 9/24/2024
 City/Town State Zip Code Date of Inspection

D. System Information (cont.)

2. Commercial/Industrial Flow Conditions:

Type of Establishment: _____

Design flow (based on 310 CMR 15.203): _____
 Gallons per day (gpd)

Basis of design flow (seats/persons/sq.ft., etc.): _____

Grease trap present? Yes No

Water treatment unit present? Yes No

If yes, discharges to: _____

Industrial waste holding tank present? Yes No

Non-sanitary waste discharged to the Title 5 system? Yes No

Water meter readings, if available: _____

Last date of occupancy/use: _____
 Date *Shared meter*

Other (describe below):

3. Pumping Records:

Source of information: pumps every spring

Was system pumped as part of the inspection? Yes No

If yes, volume pumped: _____
 gallons

How was quantity pumped determined? _____

Reason for pumping: _____



Commonwealth of Massachusetts
Title 5 Official Inspection Form
 Subsurface Sewage Disposal System Form - Not for Voluntary Assessments

950 Falmouth Road units 1-5

Property Address

South Cape Resort - Latour Group

Owner's Name

Mashpee

Ma

02649

9/24/2024

City/Town

State

Zip Code

Date of Inspection

Owner information is required for every page.

D. System Information (cont.)

4. Type of System:

- Septic tank, distribution box, soil absorption system
- Single cesspool
- Overflow cesspool
- Privy
- Shared system (yes or no) (if yes, attach previous inspection records, if any)
- Innovative/Alternative technology. Attach a copy of the current operation and maintenance contract (to be obtained from system owner) and a copy of latest inspection of the I/A system by system operator under contract
- Tight tank. Attach a copy of the DEP approval.
- Other (describe):

Approximate age of all components, date installed (if known) and source of information:

1973

Were sewage odors detected when arriving at the site?

Yes No

5. Building Sewer (locate on site plan):

Depth below grade:

2'
feet

Material of construction:

cast iron 40 PVC other (explain):

Distance from private water supply well or suction line:

10'
feet

Comments (on condition of joints, venting, evidence of leakage, etc.):

no signs of backing up in pipe or at inlet tee



Commonwealth of Massachusetts
Title 5 Official Inspection Form
 Subsurface Sewage Disposal System Form - Not for Voluntary Assessments

Owner information is required for every page.

950 Falmouth Road units 1-5
 Property Address
 South Cape Resort - Latour Group
 Owner's Name
 Mashpee
 City/Town
 Ma
 State
 02649
 Zip Code
 9/24/2024
 Date of Inspection

D. System Information (cont.)

6. **Septic Tank** (locate on site plan):

Depth below grade: 1
 feet

Material of construction:

- concrete metal fiberglass polyethylene other (explain)

If tank is metal, list age: _____
 years

Is age confirmed by a Certificate of Compliance? (attach a copy of certificate) Yes No

Dimensions: 2000 gallon

Sludge depth: 2"

Distance from top of sludge to bottom of outlet tee or baffle 38"

Scum thickness less than 1"

Distance from top of scum to top of outlet tee or baffle 5"

Distance from bottom of scum to bottom of outlet tee or baffle 18"

How were dimensions determined? tape and sludge judge

Comments (on pumping recommendations, inlet and outlet tee or baffle condition, structural integrity, liquid levels as related to outlet invert, evidence of leakage, etc.):
 tees in place. tank at onrml working level no major decay or visable cracks leaks



Title 5 Official Inspection Form

Subsurface Sewage Disposal System Form - Not for Voluntary Assessments

950 Falmouth Road units 1-5

Property Address

South Cape Resort - Latour Group

Owner's Name

Mashpee

Ma

02649

9/24/2024

City/Town

State

Zip Code

Date of Inspection

Owner information is required for every page.

D. System Information (cont.)

7. Grease Trap (locate on site plan):

Depth below grade:

feet

Material of construction:

concrete

metal

fiberglass

polyethylene

other (explain):

Dimensions:

Scum thickness

Distance from top of scum to top of outlet tee or baffle

Distance from bottom of scum to bottom of outlet tee or baffle

Date of last pumping:

Date

Comments (on pumping recommendations, inlet and outlet tee or baffle condition, structural integrity, liquid levels as related to outlet invert, evidence of leakage, etc.):

8. Tight or Holding Tank (tank must be pumped at time of inspection) (locate on site plan):

Depth below grade:

Material of construction:

concrete

metal

fiberglass

polyethylene

other (explain):

Dimensions:

Capacity:

gallons

Design Flow:

gallons per day



Commonwealth of Massachusetts
Title 5 Official Inspection Form
 Subsurface Sewage Disposal System Form - Not for Voluntary Assessments

Owner information is required for every page.

950 Falmouth Road units 1-5
 Property Address
 South Cape Resort - Latour Group
 Owner's Name
 Mashpee
 City/Town
 Ma
 State
 02649
 Zip Code
 9/24/2024
 Date of Inspection

D. System Information (cont.)

8. Tight or Holding Tank (cont.)

Alarm present: Yes No
 Alarm level: _____ Alarm in working order: Yes No
 Date of last pumping: _____
 Date

Comments (condition of alarm and float switches, etc.):

* Attach copy of current pumping contract (required). Is copy attached? Yes No

9. Distribution Box (if present must be opened) (locate on site plan):

Depth of liquid level above outlet invert _____

Comments (note if box is level and distribution to outlets equal, any evidence of solids carryover, any evidence of leakage into or out of box, etc.):
 system has bull run valve instead od Dbox



Commonwealth of Massachusetts
Title 5 Official Inspection Form
 Subsurface Sewage Disposal System Form - Not for Voluntary Assessments

Owner information is required for every page.

950 Falmouth Road units 1-5
 Property Address
 South Cape Resort - Latour Group
 Owner's Name
 Mashpee
 City/Town
 Ma
 State
 02649
 Zip Code
 9/24/2024
 Date of Inspection

D. System Information (cont.)

10. Pump Chamber (locate on site plan):

Pumps in working order: Yes No*
 Alarms in working order: Yes No*

Comments (note condition of pump chamber, condition of pumps and appurtenances, etc.):

* If pumps or alarms are not in working order, system is a conditional pass.

11. Soil Absorption System (SAS) (locate on site plan, excavation not required):

If SAS not located, explain why:

Type:

<input checked="" type="checkbox"/>	leaching pits	number:	<u>2</u>
<input type="checkbox"/>	leaching chambers	number:	_____
<input type="checkbox"/>	leaching galleries	number:	_____
<input type="checkbox"/>	leaching trenches	number, length:	_____
<input type="checkbox"/>	leaching fields	number, dimensions:	_____
<input type="checkbox"/>	overflow cesspool	number:	_____
<input type="checkbox"/>	innovative/alternative system		

Type/name of technology: _____



Commonwealth of Massachusetts Title 5 Official Inspection Form

Subsurface Sewage Disposal System Form - Not for Voluntary Assessments

950 Falmouth Road units 1-5

Property Address

South Cape Resort - Latour Group

Owner's Name

Mashpee

Ma

02649

9/24/2024

City/Town

State

Zip Code

Date of Inspection

Owner information is required for every page.

D. System Information (cont.)

11. Soil Absorption System (SAS) (cont.)

Comments (note condition of soil, signs of hydraulic failure, level of ponding, damp soil, condition of vegetation, etc.):

2 pits 6' x 10' with 4' stone pit #B dry, stain line within 2' of invert. Pit A dry and clean sides

12. Cesspools (cesspool must be pumped as part of inspection) (locate on site plan):

Number and configuration

Depth – top of liquid to inlet invert

Depth of solids layer

Depth of scum layer

Dimensions of cesspool

Materials of construction

Indication of groundwater inflow

Yes No

Comments (note condition of soil, signs of hydraulic failure, level of ponding, condition of vegetation, etc.):



Commonwealth of Massachusetts

Title 5 Official Inspection Form

Subsurface Sewage Disposal System Form - Not for Voluntary Assessments

950 Falmouth Road units 1-5

Property Address

South Cape Resort - Latour Group

Owner's Name

Mashpee

Ma

02649

9/24/2024

City/Town

State

Zip Code

Date of Inspection

Owner information is required for every page.

D. System Information (cont.)

13. Privy (locate on site plan):

Materials of construction:

Dimensions

Depth of solids

Comments (note condition of soil, signs of hydraulic failure, level of ponding, condition of vegetation, etc.):



Title 5 Official Inspection Form

Subsurface Sewage Disposal System Form - Not for Voluntary Assessments

950 Falmouth Road units 1-5

Property Address

South Cape Resort - Latour Group

Owner's Name

Mashpee

City/Town

Ma

State

02649

Zip Code

9/24/2024

Date of Inspection


Owner information is required for every page.

D. System Information (cont.)

14. Sketch Of Sewage Disposal System:

Provide a view of the sewage disposal system, including ties to at least two permanent reference landmarks or benchmarks. Locate all wells within 100 feet. Locate where public water supply enters the building. Check one of the boxes below:

- hand-sketch in the area below
- drawing attached separately

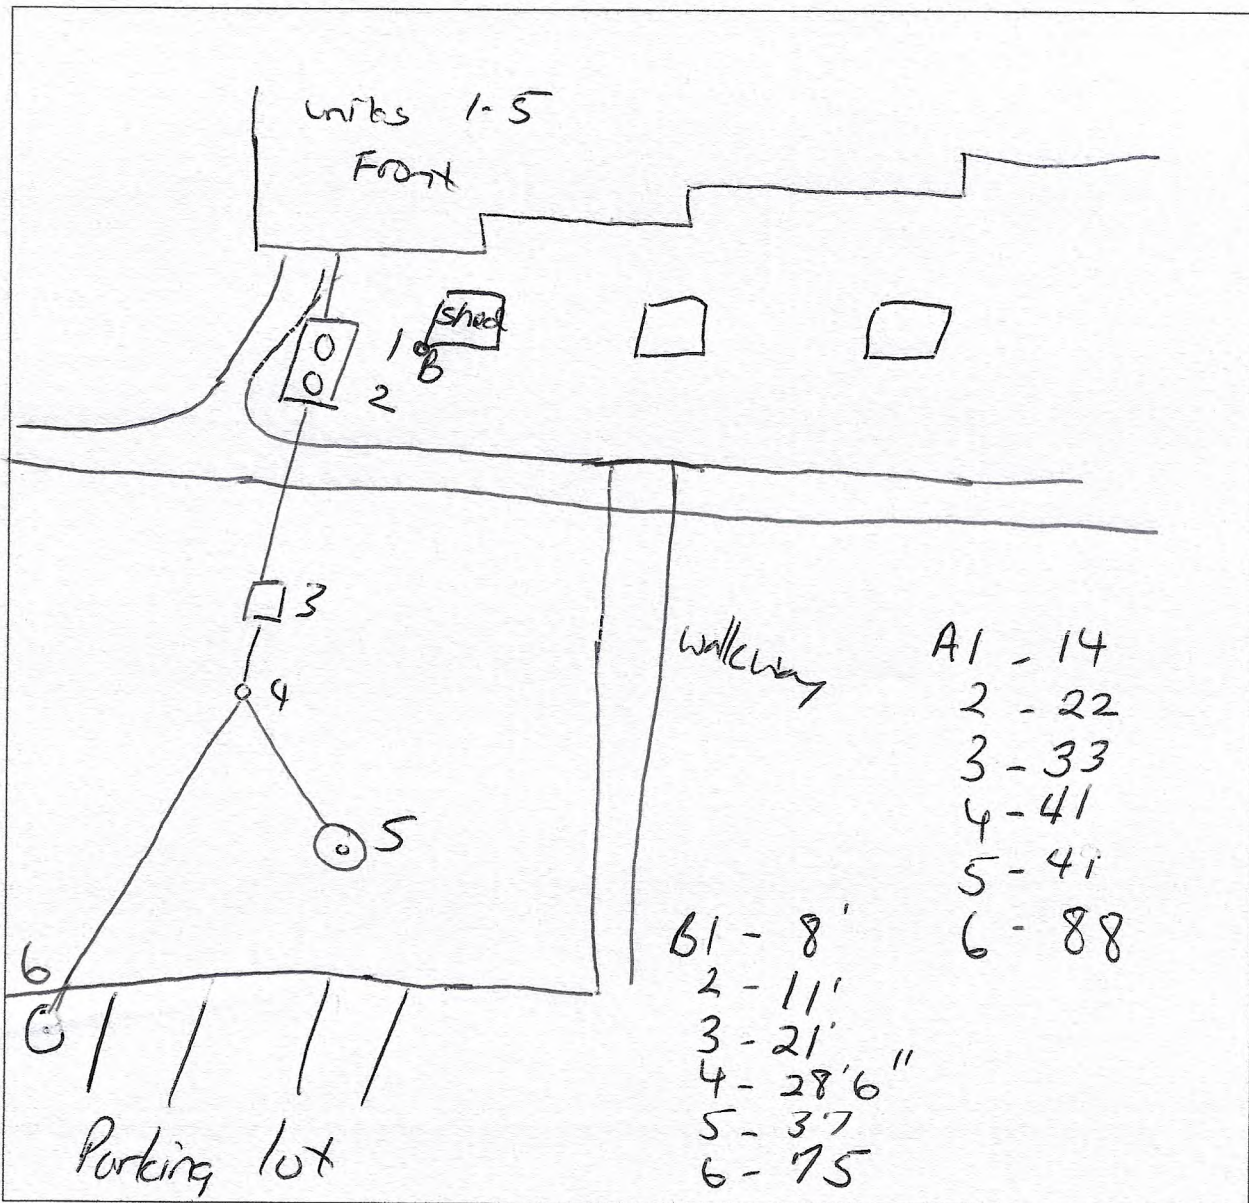



Commonwealth of Massachusetts
Title 5 Official Inspection Form
 Subsurface Sewage Disposal System Form - Not for Voluntary Assessments

Owner information is required for every page.

950 Falmouth Road units 1-5
 Property Address
 South Cape Resort - Latour Group
 Owner's Name
 Mashpee
 City/Town
 Ma
 State
 02649
 Zip Code
 9/24/2024
 Date of Inspection

D. System Information (cont.)

15. Site Exam:

- Check Slope
- Surface water
- Check cellar
- Shallow wells

Estimated depth to high ground water: 30'
 feet

Please indicate all methods used to determine the high ground water elevation:

- Obtained from system design plans on record
 If checked, date of design plan reviewed: 1973
 Date
- Observed site (abutting property/observation hole within 150 feet of SAS)
- Checked with local Board of Health - explain:

- Checked with local excavators, installers - (attach documentation)
- Accessed USGS database - explain:
town topo maps and engineered plan on file

You **must** describe how you established the high ground water elevation:

el. area of pits el. 44 bottom of test holes on property el. 14 bottom of pits 13' below grade el. 31

Before filing this Inspection Report, please see Report Completeness Checklist on next page.



Commonwealth of Massachusetts

Title 5 Official Inspection Form

Subsurface Sewage Disposal System Form - Not for Voluntary Assessments

950 Falmouth Road units 1-5

Property Address

South Cape Resort - Latour Group

Owner's Name

Mashpee

Ma

02649

9/24/2024

City/Town

State

Zip Code

Date of Inspection

Owner information is required for every page.

E. Report Completeness Checklist

Complete all applicable sections of this form inclusive of:

A. Inspector Information: Complete all fields in this section.

B. Certification: Signed & Dated and 1, 2, 3, or 4 checked

C. Inspection Summary:

1, 2, 3, or 5 completed as appropriate

4 (Failure Criteria) and 6 (Checklist) completed

D. System Information:

For 8: Tight/Holding Tank – Pumping contract attached

For 14: Sketch of Sewage Disposal System drawn on pg. 16 or attached

For 15: Explanation of estimated depth to high groundwater included



TITLE V INSPECTION CHECKLIST

950 Falmouth rd. units 1-5

The checklist below is provided as a convenient summary of the requirements in the Mashpee Board of Health Septic Inspection Regulation Part IX Section 17.00. Please complete and submit with State Inspection Form.

YES NO

1. Are you registered with the Mashpee Board of Health to perform septic inspections? There is no fee for registration.
2. Does the Soil Absorption System have 24 hours of retention / liquid capacity below the invert or effective depth? See #15.
3. Is the Soil Absorption System in failure? If yes, a Health Agent is required to verify failure in the field.
4. Is the property serviced by a Private Well? If yes, testing is required.
5. Has the private well been located from two (2) points and shown on the sketch? See #15.
6. Have risers on the inlet and outlet of Septic Tanks, Distribution Boxes, and Soil Absorption Systems been brought to within 6 inches of grade? Or, are observation ports on plastic chambers?
7. Has the driveway been shown on the sketch?
8. Has the amount of stone / capacity of the Soil Absorption System been determined?
9. Has the piping scheme been shown on the sketch?
10. Has the groundwater elevation been determined?
11. Has a violation of the 1978 or 1995 Title V Codes been identified? If yes, list violations on the inspection report.
12. Has the Septic Tank, Grease Trap, Pump Chamber, and/or Distribution Box been identified H-10 or H20 for vehicle loading?
13. For property transfer inspections, does the Soil Absorption System have four (4) feet to estimated seasonally high groundwater?
14. Is the Septic Tank 30 years old or older? If yes, circle all that apply below. If you answer **yes** to any of the below criteria, the septic tank shall be considered a Conditional Pass.

- a) If the septic tank has not been pumped in the previous two (2) years, the tank must be pumped after initial solids levels are determined, so that the interior of the tank may be inspected and maintenance may be performed.
- b) One inch loss of concrete due to decay and/or crumbling at waterline or surfaces of the tank. The tees may be replaced with a permit if the remainder of the tank is considered sound.
- c) Inlet and/or outlet tees or baffle walls have "fallen off" due to decay.
- d) Cracks are observed extending through the wall and/or top of the tank. Observed bulging or sagging walls or ceiling of tank.
- e) Exposed reinforcement bars indicated by rust-colored lines inside the septic tank.
- f) The tank is leaking as observed by a liquid level (not expected by evaporation - greater than 4") below the outlet invert. All H-10 septic tanks buried greater than four (4) feet below grade must be replaced.

15. All repairs identified in a Conditional Pass or Needs Further Evaluation Report, or per the Cesspool Regulation must be repaired prior to the sale of the property. If the repair is not performed prior to the sale, variance relief is required.

All tanks pumped yearly
